CROSS FLORIDA GREENWAY - DESIGN & PERMITTING SCHEDULE

Kimley»Horn

ID	Task Name	Duration	Start	Finish
1	CROSS FLORIDA GREENWAY	252 days	Tue 2/3/26	Wed 1/20/27
2	Design and Permitting	252 days	Tue 2/3/26	Wed 1/20/27
3	60% Design and Plans	100 days	Tue 2/3/26	Mon 6/22/26
4	Contract Amendment	47 days	Tue 2/24/26	Wed 4/29/26
5	60% Design Submittal to County, Sun Trail, CSX/FL Northern, SJRWMD, Utility Agencies	0 days	Tue 6/23/26	Tue 6/23/26
6	60% Design Review by Agencies	23 days	Wed 6/24/26	Fri 7/24/26
7	60% Comment Resolution Meeting with County	0 days	Thu 7/30/26	Thu 7/30/26
8	90% Design and Plans	62 days	Thu 7/30/26	Fri 10/23/26
9	90% Design Submittal to County, Sun Trail, CSX/FL Northern, SJRWMD, Utility Agencies	0 days	Mon 10/26/26	Mon 10/26/26
10	90% Design Review by Agencies	23 days	Tue 10/27/26	Thu 11/26/26
11	90% Comment Resolution Meeting with County	0 days	Mon 12/7/26	Mon 12/7/26
12	100% Design and Plans	33 days	Mon 12/7/26	Wed 1/20/27
13	100% Design Submittal to County, Sun Trail, CSX/FL Northern, Utility Agencies	0 days	Wed 1/20/27	Wed 1/20/27

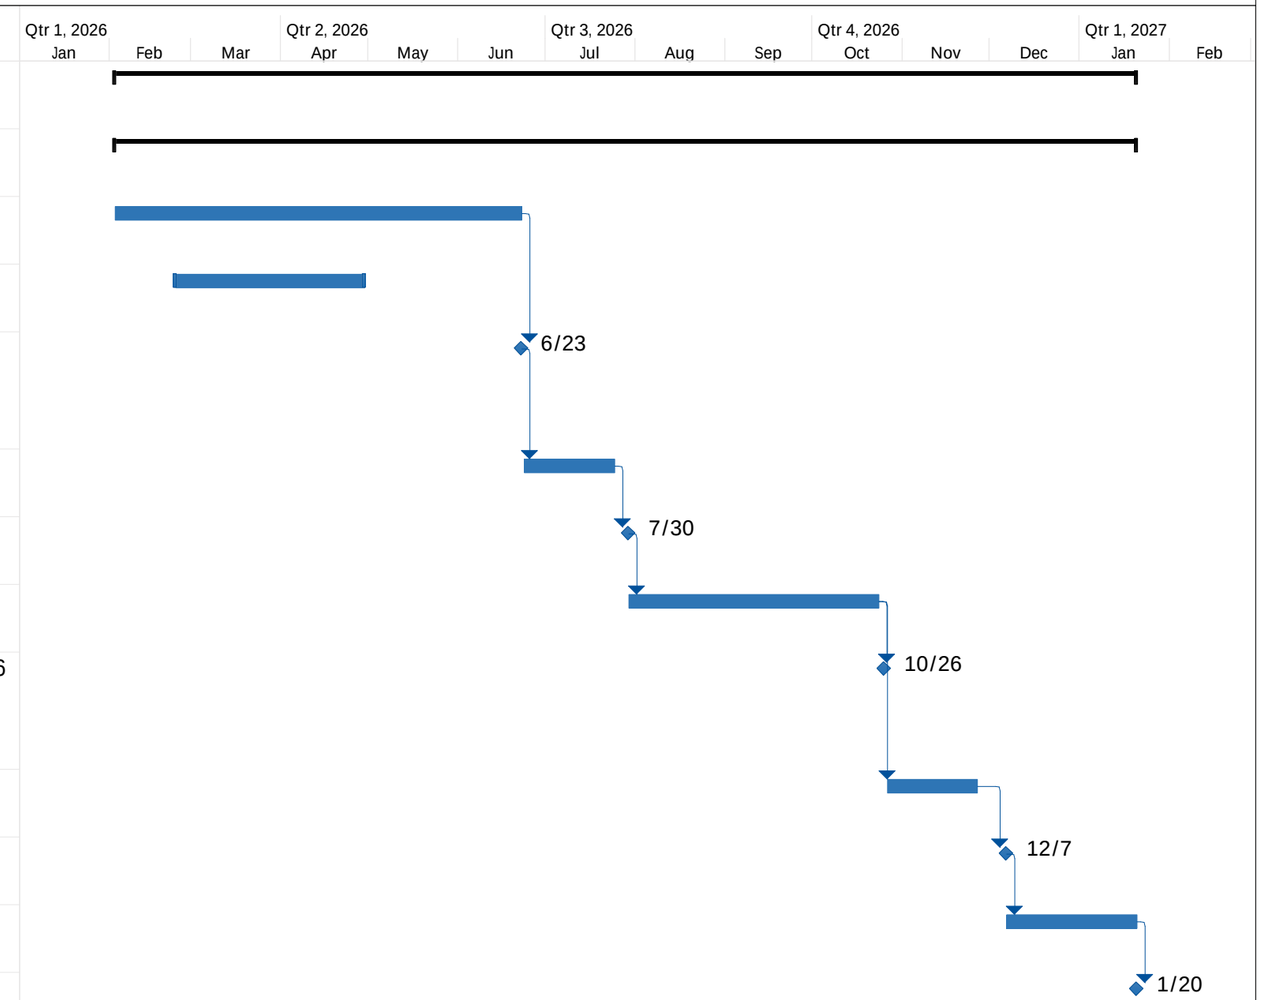

Project: Cross FL Greenway.mp
Date: Mon 5/4/26

Task Milestone Summary
